

SE LAB-2

Ayushman Dey
PES2UG24CS102


- **Jira backlog with Epics and User Stories and Story Points:**

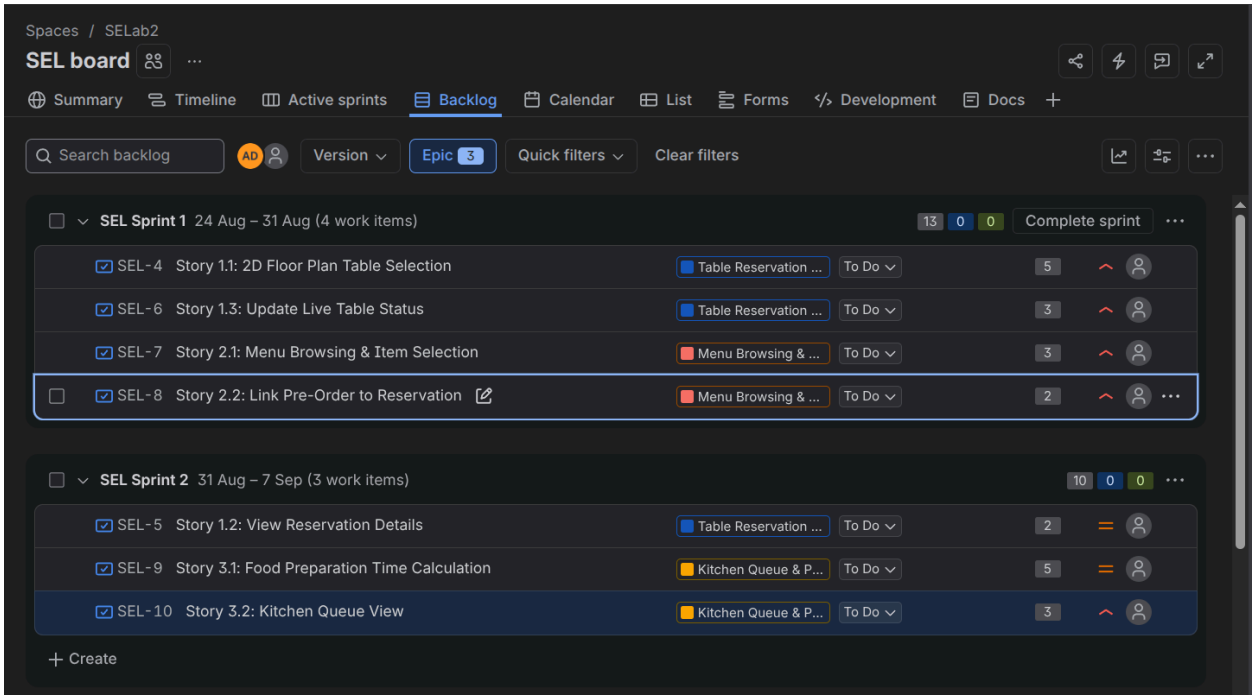


- **Active Sprint Board:**

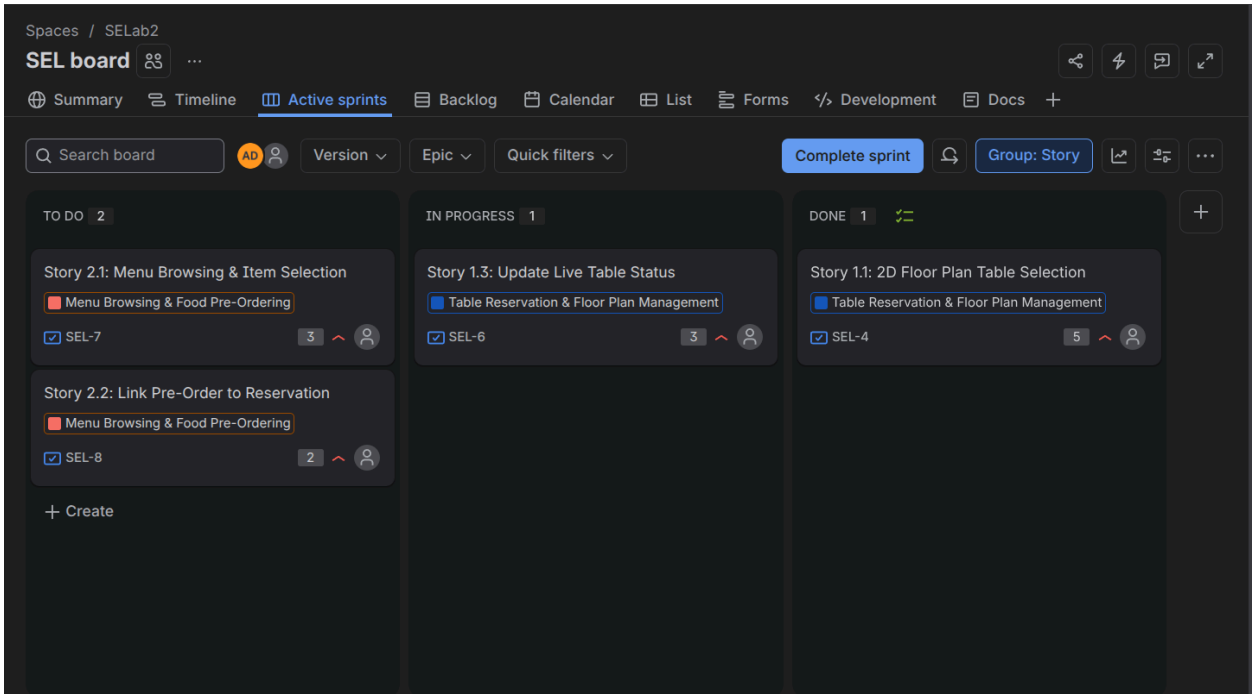

- **Burndown Chart:**

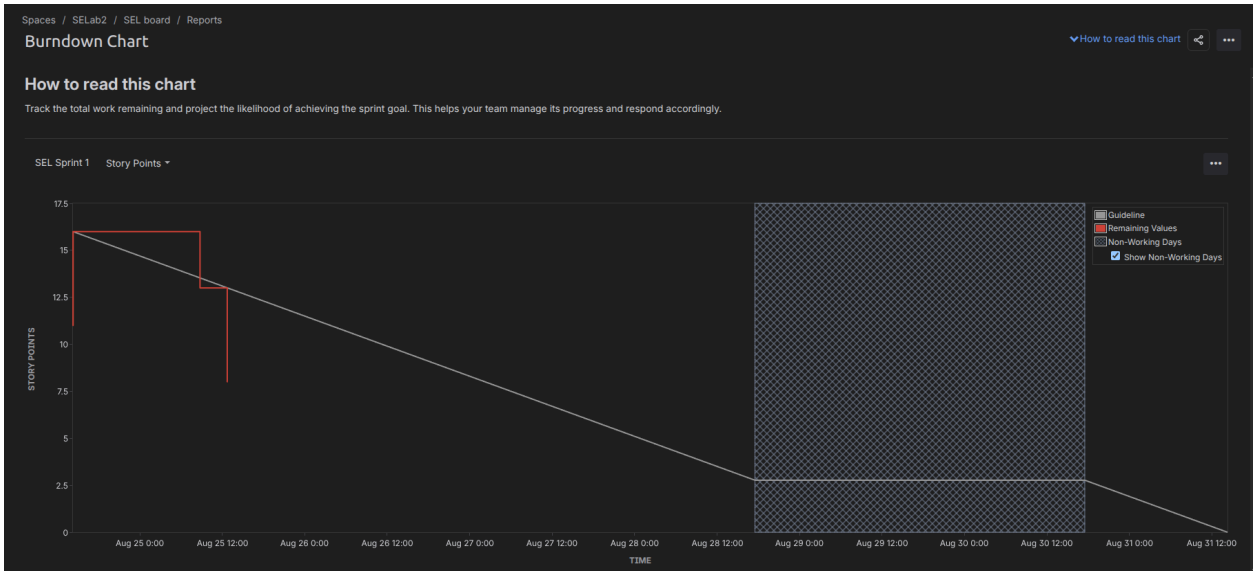

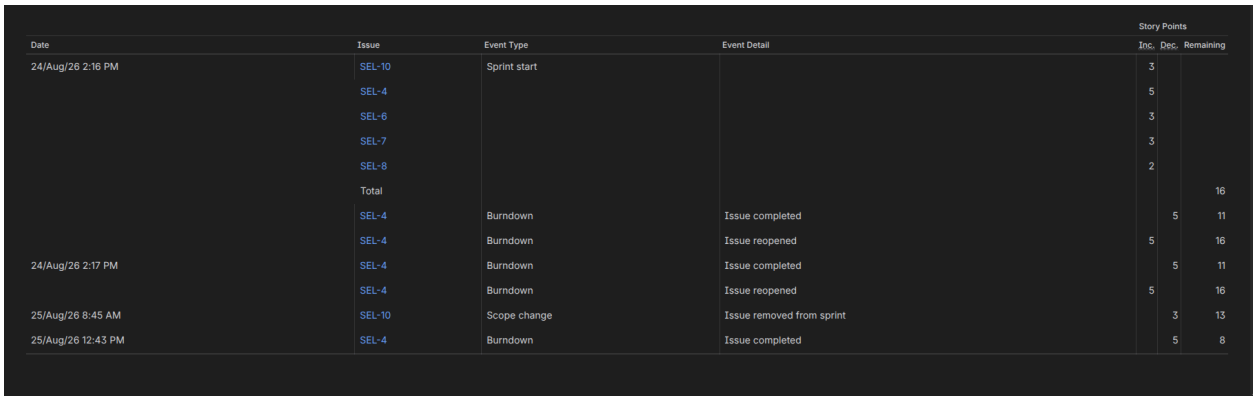

Date	Issue	Event Type	Event Detail	Story Points Inc.	Dec.	Remaining
24/Aug/26 2:16 PM	SEL-10	Sprint start		3		
	SEL-4			5		
	SEL-6			3		
	SEL-7			3		
	SEL-8			2		
	Total					16
	SEL-4	Burndown	Issue completed		5	11
	SEL-4	Burndown	Issue reopened	5		16
24/Aug/26 2:17 PM	SEL-4	Burndown	Issue completed		5	11
	SEL-4	Burndown	Issue reopened	5		16
25/Aug/26 8:45 AM	SEL-10	Scope change	Issue removed from sprint		3	13
25/Aug/26 12:43 PM	SEL-4	Burndown	Issue completed		5	8

• REFLECTION QUESTIONS:

1. Did your estimations reflect the actual effort?

The estimations reflected the actual effort well. Using the Fibonacci scale helped size the tasks properly based on their complexity. For example, developing the interactive 2D floor plan is a complex task, so it received 5 story points. On the other hand, creating a simple screen to view reservation details is much easier and was given 2 points. This point system matched how long it would realistically take to build these features.

2. Was your backlog well-prioritized?

Yes, the backlog was prioritized logically based on what the application needs to function. Core features like table booking and the main food pre-ordering system were set as High priority for the first sprint. Secondary features, such as viewing the kitchen queue and estimating prep times, were assigned to Sprint 2. This kept the focus on building the most important parts of the app first.

3. How did your simulated sprint align with your plan?

The simulated sprint followed the initial plan smoothly. I moved the high-priority tasks into Sprint 1, started the sprint, and shifted the work items from the To Do column, to In Progress, and then to Done. Breaking the larger epics into smaller user stories worth 2 to 5 points made it easier to manage the workload and move things across the board without getting stuck on one large task.

4. What insights did the burndown chart give about your team's capacity?

The burndown chart showed a steady downward trend along the grey guideline as tasks were completed. This indicates that the team capacity was managed well and the work was broken down into appropriate sizes. If the red line had stayed flat for a long time or dropped all at once at the end, it would mean the tasks were too large or the story points were estimated incorrectly.
